ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
0		**ProcureEase DEVELOPMENT PLAN**	**52 days**	**Mon 2/19/18**	**Tue 5/1/18**		
1		**Planning**	**3.63 days**	**Mon 2/19/18**	**Thu 2/22/18**		
2		Preparing mock up for phase one, Technical and functional spec	2 days	Mon 2/19/18	Tue 2/20/18		Ayo,Muyiwa,Cosma
3		Planning for Development	2 days	Mon 2/19/18	Tue 2/20/18	2SS	Ayo,Muyiwa,Grace,
4		Demo of final mock up, Technical specs and process flow for Phase 1	1 hr	Wed 2/21/18	Wed 2/21/18	3	Procureease team
5		Fixing of feedbacks from demo	1.5 days	Wed 2/21/18	Thu 2/22/18	4	Ayo,Muyiwa
6		**Development**	**48 days**	**Mon 2/19/18**	**Wed 4/25/18**		
7		**Development and connecting Api Front end**	**48 days**	**Mon 2/19/18**	**Wed 4/25/18**	**3SS**	
8		Sign up page	3 days	Mon 2/19/18	Wed 2/21/18		Ayo
9		Sign in page	2 days	Thu 2/22/18	Fri 2/23/18	8	Ayo
10		Creating the dashboard interface	5 days	Mon 2/26/18	Fri 3/2/18	9	Grace,Ayo
11		Linking all pages to the dashboard	2 days	Mon 3/5/18	Tue 3/6/18	10	Ayo

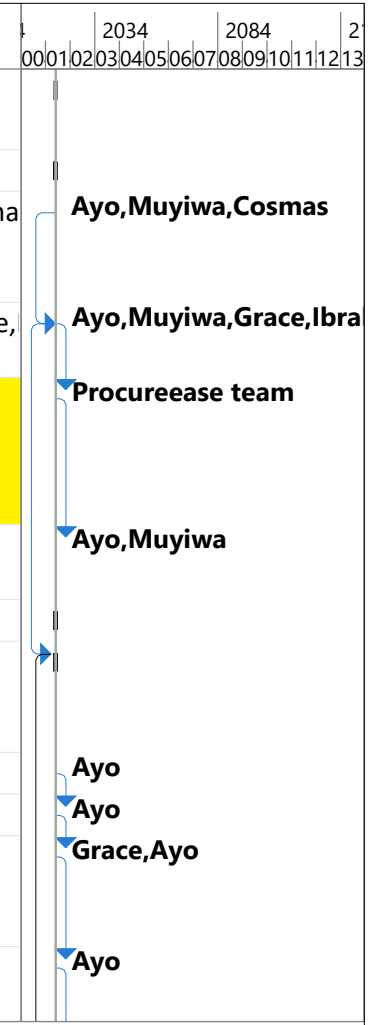

Project: ProcureEase DEVELOPM
Date: Fri 3/9/18

Task	Inactive Summary	External Tasks	
Split	Manual Task	External Milestone	
Milestone	Duration-only	Deadline	
Summary	Manual Summary Rollup	Progress	
Project Summary	Manual Summary	Manual Progress	
Inactive Task	Start-only		
Inactive Milestone	Finish-only		

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
12		Create new user and assign role page	4 days	Wed 3/7/18	Mon 3/12/18	11	Grace,Ayo
13		MDA Profile page	3 days	Tue 3/13/18	Thu 3/15/18	12	Grace,Ayo
14		New Procurement Plan page	5 days	Fri 3/16/18	Thu 3/22/18	13	Ayo,Grace
15		Procurement Management plan	8 days	Fri 3/23/18	Tue 4/3/18	14	Ayo,Grace
16		Tender page	3 days	Wed 4/4/18	Fri 4/6/18	15	Ayo,Grace
17		Advert page	3 days	Mon 4/9/18	Wed 4/11/18	16	Ayo,Grace
18		Congrats page	3 days	Thu 4/12/18	Mon 4/16/18	17	Ayo,Grace
19		Review page	3 days	Tue 4/17/18	Thu 4/19/18	18	Ayo,Grace
20		Settings page	2 days	Fri 4/20/18	Mon 4/23/18	19	
21		Forget Password	2 days	Tue 4/24/18	Wed 4/25/18	20	Ayo,Grace
22		End of development	0 days	Wed 4/25/18	Wed 4/25/18	21	
23		**Development Back end**	**31 days**	**Mon 2/19/18**	**Mon 4/2/18**		
24		Preparing Environment	2 days	Mon 2/19/18	Tue 2/20/18	7SS	Muyiwa

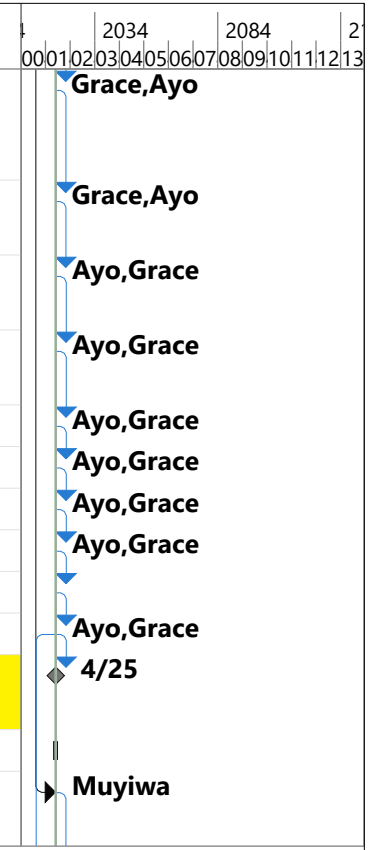

Project: ProcureEase DEVELOPM
Date: Fri 3/9/18

Task	Inactive Summary	External Tasks	
Split	Manual Task	External Milestone	
Milestone	Duration-only	Deadline	
Summary	Manual Summary Rollup	Progress	
Project Summary	Manual Summary	Manual Progress	
Inactive Task	Start-only		
Inactive Milestone	Finish-only		

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
25		Creating Api for user management (Sign in, Sign up, forget password, Email notification, user profile, Admin sign up others,	7 days	Wed 2/21/18	Thu 3/1/18	24	Muyiwa
26		Creating Api for Procurement Management	7 days	Fri 3/2/18	Mon 3/12/18	25	Muyiwa
27		Creating Api for Homepage	7 days	Tue 3/13/18	Wed 3/21/18	26	Muyiwa
28		Creating Api for Upload tender page	3 days	Thu 3/22/18	Mon 3/26/18	27	Muyiwa
29		Creating API for Advert management	5 days	Tue 3/27/18	Mon 4/2/18	28	Muyiwa
30		End of development	0 days	Mon 4/2/18	Mon 4/2/18	29	
31		Demo of completed procureEase	1 day	Tue 4/24/18	Tue 4/24/18	21SS	Grace
32		Fixing of feedbacks	5 days	Wed 4/25/18	Tue 5/1/18	31	Ayo,Muyiwa,Grace
33		Feedback Done	0 hrs	Wed 4/25/18	Wed 4/25/18	32SS	
34		Demo of Phase one	1 day	Wed 4/25/18	Wed 4/25/18	33	Ayo
35		Fixing of feedbacks	2 days	Thu 4/26/18	Fri 4/27/18	34	Muyiwa,Ayo,Grace
36		Demo of Fixed Phase one	1 day	Mon 4/30/18	Mon 4/30/18	35	Ayo,Grace

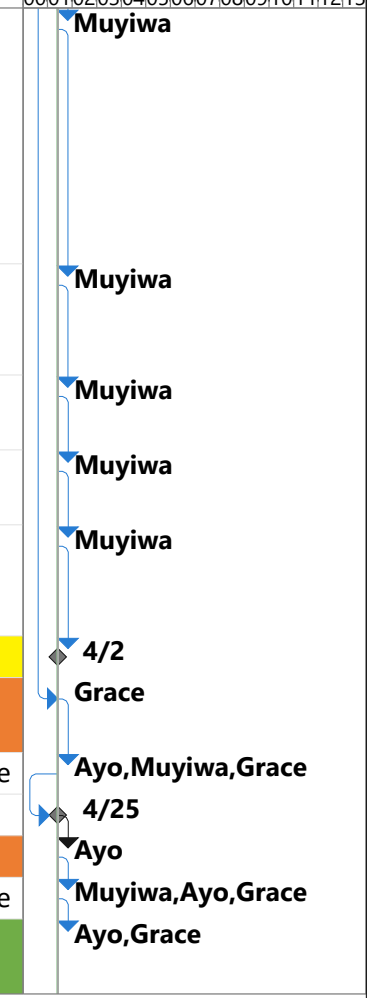

Project: ProcureEase DEVELOPM
Date: Fri 3/9/18

Task	Inactive Summary	External Tasks	
Split	Manual Task	External Milestone	
Milestone	Duration-only	Deadline	
Summary	Manual Summary Rollup	Progress	
Project Summary	Manual Summary	Manual Progress	
Inactive Task	Start-only		
Inactive Milestone	Finish-only		
